



June
2013

PATRIARCAT 482

Progress Report

CONTENTS

1. INTRODUCTION
 - a. Introduction
 - b. Project brief
 - c. Project particulars

2. EXECUTIVE SUMMARY
 - a. Project construction main data

3. PROGRESS OVER VIEW
 - a. Progress of works
 - b. Safety Management

4. PHOTOS

1.

a. INTRODUCTION

The progress report is an assessment that takes place during a project or process, that conveys details such as what sub-goals have been accomplished, what resources have been expended, what problems have been encountered, and whether the project or process is expected to be completed on time and within budget.

It is intended to be a proactive decision- making document; a separate section on actions and alerts has been highlighted for each action along the due dates.

This report also provides a streamlined analysis of the actual, planned and forecasted events of the project.

The executive summary will provide brief information on the project status.

The general progress overview will provide details on progress achieved to date on the project. The progress that is reported encompasses time, cost, quality, risk, scope, procurement, resources, and safety management.

b. PROJECT BRIEF

PATRIARCAT RESIDENCE 482 (PR), is located in the prestigious location of Batrakiyeh in Beirut city. Its proximity to Solidere, Verdun, Hamra and Achrafieh is one of its biggest assets, as they are easily reached and the Rafic Hariri International Airport is **less than 15 minutes away via the highway. All of Beirut' s amenities and all of Lebanon are readily accessible to Patriarcats Tower' s residents.**

Below are some views of the project' s exterior and interior views:





01

PERSPECTIVE VIEW

A09

PATRIARCAS
TOWERS 482






c. PROJECT PARTICULARS

Project Title:	Patriarcat Residence 482	PR
Location:	Beirut, Lebanon	
Developer:	BMI SAL	BMI
Main Contractor:	Dolmen Contracting	DC
Consultant:	MN- Line Architects	MNL
MEP Subcontractor:	AlBonian Group	BG

2. EXECUTIVE SUMMARY

a. Project Construction Main Data

Project name	
Project Budget	4,500,000 \$
Project Start Date	October 2011
Project Finish Date	December 2013
Project Duration	820 days
Days Elapsed	575
Percentage Of days elapsed	70 %

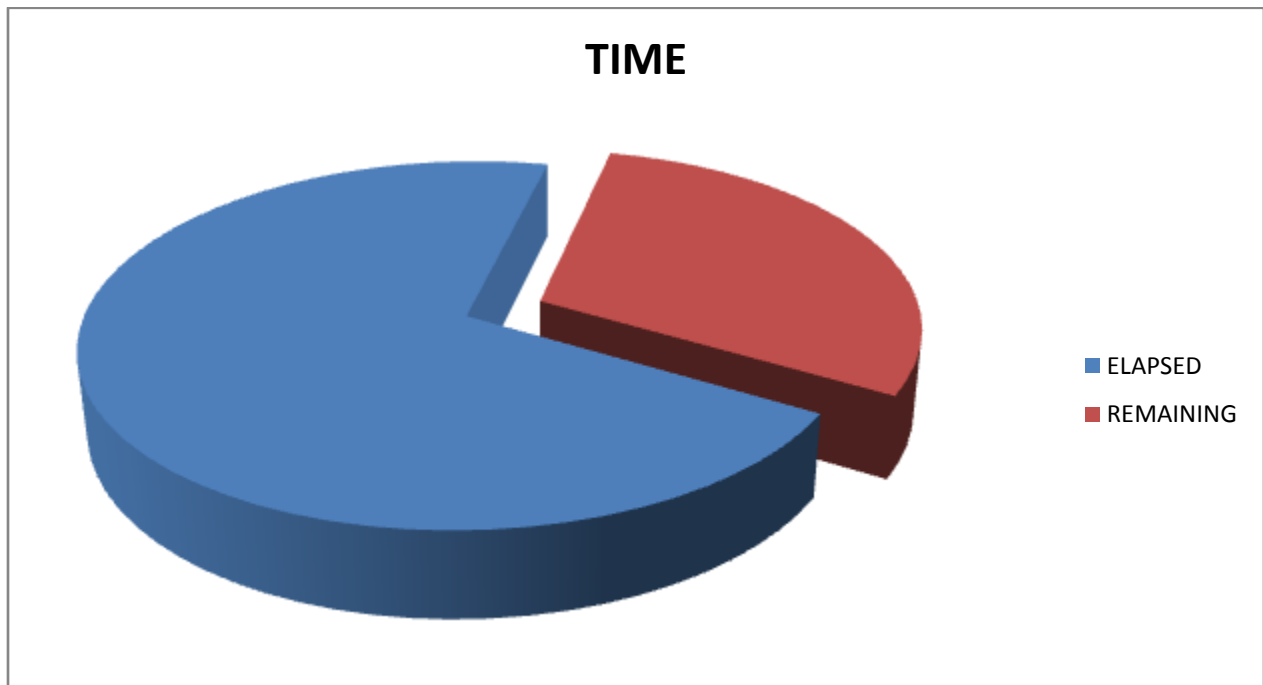



3. PROGRESS OVERVIEW

a. Progress of Works

FLR	DIVISION	TASK	BLOCK A	BLOCK B	COMMENTS
Basement 2	Concrete Works	Columns	100%	100%	
		Slabs	100%	100%	
	Finishes	Masonry	100%	100%	
		Lintels and jambs	100%	100%	
		Wood works - subframes	0%	0%	
		Metal works - subframes	0%	0%	
		Plastering	80%	80%	
		Paint - ceilings	0%	0%	
		Floors tiling	0%	0%	
		Paint works – putty+primer	0%	0%	
		Metal works - doors & windows	0%	0%	
		Wood works - joinery & doors	0%	0%	
		Wood works -	0%	0%	
		Polishing works	0%	0%	
		Paint works - final coat	0%	0%	
		Epoxy - final coat	0%	0%	
	MEP	Drainage system UPVC	40%	40%	
		Duct installation	0%	0%	
		Cables and wires pulling	40%	40%	
		Fans	0%	0%	
		Tanks	0%	0%	
		Pumps	0%	0%	
		Wiring devices installation	40%	40%	
Lighting fixtures installation		10%	10%		
Panel Board installation		10%	10%		
Mechanical functional test		0%	0%		
Electrical functional test	0%	0%			

Basement 1	Concrete Works	Columns	100%	100%	
		Slabs	100%	100%	
	Finishes	Masonry	0%	0%	
		Lintels and jambs	0%	0%	
		Wood works - subframes	0%	0%	
		Metal works - subframes	0%	0%	
		Plastering	80%	80%	
		Paint - ceilings	0%	0%	
		Floors tiling	0%	0%	
		Paint works – putty+primer	0%	0%	
		Metal works - doors & windows	0%	0%	
		Wood works - joinery & doors	0%	0%	
		Wood works -	0%	0%	
		Polishing works	0%	0%	
		Paint works - final coat	0%	0%	
		Epoxy - final coat	0%	0%	
	MEP	Drainage system UPVC	40%	40%	
		Duct installation	0%	0%	
		Cables and wires pulling	0%	0%	
		Fans	0%	0%	
Wiring devices installation		10%	10%		
Lighting fixtures installation		10%	10%		
Panel Board installation		0%	0%		
Mechanical functional test		0%	0%		
Electrical functional test		0%	0%		

Ground Floor	Concrete Works	Columns	100%	100%	
		Slabs	100%	100%	
	Finishes	Masonry	40%	40%	
		Lintels and jambs	40%	40%	
		Wood works - subframes	0%	0%	
		Metal works - subframes	0%	0%	
		Plastering	10%	10%	
		Paint - ceilings	0%	0%	
		Walls tiling (WCs and Kitchen)	0%	0%	
		Waterproofing - wet areas	0%	0%	
		False Ceilings	0%	0%	
		Floors tiling	0%	0%	
		Paint works – putty+primer	0%	0%	
		Metal works - doors & windows	0%	0%	
		Wood works - joinery & doors	0%	0%	
		Wood works - kitchens & closets	0%	0%	
		Polishing works	0%	0%	
		Paint works - final coat	0%	0%	
	Epoxy - final coat	0%	0%		
	MEP	Drainage system UPVC	40%	40%	
		PPR - wet areas	0%	0%	
		GS - dry areas	0%	0%	
		Duct installation	0%	0%	
		Cables and wires pulling	40%	40%	
		Fans	0%	0%	
		Tanks	0%	0%	
		Pumps	0%	0%	
		Sanitary fixtures installation	0%	0%	
Wiring devices installation		40%	40%		
Lighting fixtures installation		0%	0%		
Panel Board installation		0%	0%		
Mechanical functional test	0%	0%			
Electrical functional test	0%	0%			

1st Floor	Concrete Works	Columns	100%	100%	
		Slabs	100%	100%	
	Finishes	Masonry	100%	100%	
		Lintels and jambs	100%	100%	
		Wood works - subframes	100%	100%	
		Metal works - subframes	0%	0%	
		Plastering	100%	100%	
		Paint - ceilings	70%	30%	
		Walls tiling (WCs and Kitchen)	0%	0%	
		Waterproofing - wet areas	20%	20%	
		False Ceilings	50%	0%	
		Floors tiling	0%	0%	
		Paint works – putty+primer	70%	70%	
		Metal works - doors & windows	0%	0%	
		Wood works - joinery & doors	50%	50%	
		Wood works - kitchens & closets	0%	0%	
		Polishing works	0%	0%	
		Paint works - final coat	0%	0%	
	Epoxy - final coat	0%	0%		
	MEP	Drainage system UPVC	70%	70%	
		PPR - wet areas	60%	60%	
		GS - dry areas	60%	60%	
		Duct installation	100%	100%	
		Cables and wires pulling	90%	90%	
		Fans	0%	0%	
		Sanitary fixtures installation	0%	0%	
		Wiring devices installation	80%	80%	
		Lighting fixtures installation	0%	0%	
Panel Board installation		0%	0%		
Mechanical functional test		50%	50%		
Electrical functional test		0%	0%		

2nd Floor	Concrete Works	Columns	100%	100%	
		Slabs	100%	100%	
	Finishes	Masonry	100%	100%	
		Lintels and jambs	100%	100%	
		Wood works - subframes	100%	100%	
		Metal works - subframes	80%	80%	
		Plastering	100%	100%	
		Paint - ceilings	30%	30%	
		Floors grinding	0%	0%	
		Walls tiling (WCs and Kitchen)	0%	0%	
		Waterproofing - wet areas	80%	80%	
		False Ceilings	0%	0%	
		Floors tiling	80%	0%	
		Paint works – putty+primer	50%	50%	
		Metal works - doors & windows	0%	0%	
		Wood works - joinery & doors	50%	50%	
		Wood works - kitchens & closets	0%	0%	
		Polishing works	0%	0%	
		Paint works - final coat	0%	0%	
		Epoxy - final coat	0%	0%	
	MEP	Drainage system UPVC	70%	70%	
		PPR - wet areas	0%	0%	
		GS - dry areas	0%	0%	
		Duct installation	100%	100%	
		Cables and wires pulling	80%	80%	
		Fans	0%	0%	
		Sanitary fixtures installation	0%	0%	
		Wiring devices installation	50%	50%	
Lighting fixtures installation		40%	40%		
Panel Board installation		0%	0%		
Mechanical functional test		0%	0%		
Electrical functional test		0%	0%		

3rd Floor	Concrete Works	Columns	100%	100%	
		Slabs	100%	100%	
	Finishes	Masonry	100%	100%	
		Lintels and jambs	100%	100%	
		Wood works - subframes	100%	100%	
		Metal works - subframes	0%	0%	
		Plastering	100%	100%	
		Paint - ceilings	20%	20%	
		Floors grinding	0%	0%	
		Walls tiling (WCs and Kitchen)	0%	0%	
		Waterproofing - wet areas	0%	0%	
		False Ceilings	0%	0%	
		Floors tiling	0%	0%	
		Paint works – putty+primer	30%	30%	
		Metal works - doors & windows	0%	0%	
		Wood works - joinery & doors	0%	0%	
		Wood works - kitchens & closets	0%	0%	
		Polishing works	0%	0%	
		Paint works - final coat	0%	0%	
		Epoxy - final coat	0%	0%	
	MEP	Drainage system UPVC	50%	50%	
		PPR - wet areas	0%	0%	
		GS - dry areas	0%	0%	
		Duct installation	0%	0%	
		Cables and wires pulling	0%	0%	
		Fans	0%	0%	
		Sanitary fixtures installation	0%	0%	
Wiring devices installation		0%	0%		
Lighting fixtures installation		40%	40%		
Panel Board installation		0%	0%		
Mechanical functional test		0%	0%		
Electrical functional test	0%	0%			

4th Floor	Concrete Works	Columns	100%	100%	
		Slabs	100%	100%	
	Finishes	Masonry	100%	100%	
		Lintels and jambs	100%	100%	
		Wood works - subframes	100%	100%	
		Metal works - subframes	0%	0%	
		Plastering	100%	100%	
		Paint - ceilings	10%	10%	
		Walls tiling (WCs and Kitchen)	0%	0%	
		Waterproofing - wet areas	0%	0%	
		False Ceilings	0%	0%	
		Floors tiling	0%	0%	
		Paint works – putty+primer	20%	20%	
		Metal works - doors & windows	0%	0%	
		Wood works - joinery & doors	0%	0%	
		Wood works - kitchens & closets	0%	0%	
		Polishing works	0%	0%	
		Paint works - final coat	0%	0%	
	Epoxy - final coat	0%	0%		
	MEP	Drainage system UPVC	70%	70%	
		PPR - wet areas	0%	0%	
		GS - dry areas	0%	0%	
		Duct installation	100%	100%	
		Cables and wires pulling	0%	0%	
		Fans	0%	0%	
		Sanitary fixtures installation	0%	0%	
		Wiring devices installation	50%	50%	
Lighting fixtures installation		0%	0%		
Panel Board installation		0%	0%		
Mechanical functional test		0%	0%		
Electrical functional test	0%	0%			

5th Floor	Concrete Works	Columns	100%	100%	
		Slabs	100%	100%	
	Finishes	Masonry	100%	100%	
		Lintels and jambs	100%	100%	
		Wood works - subframes	100%	100%	
		Metal works - subframes	0%	0%	
		Plastering	100%	100%	
		Paint - ceilings	10%	10%	
		Walls tiling (WCs and Kitchen)	0%	0%	
		Waterproofing - wet areas	0%	0%	
		False Ceilings	10%	10%	
		Floors tiling	0%	0%	
		Paint works – putty+primer	0%	0%	
		Metal works - doors & windows	0%	0%	
		Wood works - joinery & doors	0%	0%	
		Wood works - kitchens & closets	0%	0%	
		Polishing works	0%	0%	
		Paint works - final coat	0%	0%	
	Epoxy - final coat	0%	0%		
	MEP	Drainage system UPVC	80%	80%	
		PPR - wet areas	0%	0%	
		GS - dry areas	0%	0%	
		Duct installation	100%	100%	
Cables and wires pulling		40%	40%		
Fans		0%	0%		
Sanitary fixtures installation		0%	0%		
Wiring devices installation		100%	100%		
Lighting fixtures installation		0%	0%		
Panel Board installation		0%	0%		
Mechanical functional test		0%	0%		
Electrical functional test	0%	0%			

6th Floor	Concrete Works	Columns	100%	100%	
		Slabs	100%	100%	
	Finishes	Masonry	100%	100%	
		Lintels and jambs	100%	100%	
		Wood works - subframes	100%	100%	
		Metal works - subframes	0%	0%	
		Plastering	100%	100%	
		Paint - ceilings	5%	5%	
		Floors grinding	0%	0%	
		Walls tiling (WCs and Kitchen)	0%	0%	
		Waterproofing - wet areas	0%	0%	
		False Ceilings	0%	0%	
		Floors tiling	0%	0%	
		Paint works – putty+primer	0%	0%	
		Metal works - doors & windows	0%	0%	
		Wood works - joinery & doors	0%	0%	
		Wood works - kitchens & closets	0%	0%	
		Polishing works	0%	0%	
		Paint works - final coat	0%	0%	
		Epoxy - final coat	0%	0%	
	MEP	Drainage system UPVC	80%	80%	
		PPR - wet areas	0%	0%	
		GS - dry areas	0%	0%	
		Duct installation	100%	100%	
		Cables and wires pulling	60%	60%	
		Fans	0%	0%	
		Sanitary fixtures installation	0%	0%	
Wiring devices installation		100%	100%		
Lighting fixtures installation		0%	0%		
Panel Board installation		0%	0%		
Mechanical functional test		0%	0%		
Electrical functional test	0%	0%			

7th Floor	Concrete Works	Columns	100%	100%	
		Slabs	100%	100%	
	Finishes	Masonry	100%	100%	
		Lintels and jambs	100%	100%	
		Wood works - subframes	100%	100%	
		Metal works - subframes	0%	0%	
		Plastering	100%	100%	
		Paint - ceilings	0%	0%	
		Walls tiling (WCs and Kitchen)	0%	0%	
		Waterproofing - wet areas	0%	0%	
		False Ceilings	0%	0%	
		Floors tiling	0%	0%	
		Paint works – putty+primer	0%	0%	
		Metal works - doors & windows	0%	0%	
		Wood works - joinery & doors	0%	0%	
		Wood works - kitchens & closets	0%	0%	
		Polishing works	0%	0%	
		Paint works - final coat	0%	0%	
	Epoxy - final coat	0%	0%		
	MEP	Drainage system UPVC	70%	70%	
		PPR - wet areas	0%	0%	
		GS - dry areas	0%	0%	
		Duct installation	60%	60%	
		Cables and wires pulling	60%	60%	
		Fans	0%	0%	
		Tanks	0%	0%	
		Pumps	0%	0%	
		Sanitary fixtures installation	0%	0%	
Wiring devices installation		100%	100%		
Lighting fixtures installation		0%	0%		
Panel Board installation		0%	0%		
Mechanical functional test		0%	0%		
Electrical functional test		0%	0%		

8th Floor	Concrete Works	Columns	100%	100%	
		Slabs	100%	100%	
	Finishes	Masonry	100%	100%	
		Lintels and jambs	100%	100%	
		Wood works - subframes	100%	100%	
		Metal works - subframes	0%	0%	
		Plastering	100%	100%	
		Paint - ceilings	0%	0%	
		Walls tiling (WCs and Kitchen)	0%	0%	
		Waterproofing - wet areas	0%	0%	
		False Ceilings	0%	0%	
		Floors tiling	0%	0%	
		Paint works – putty+primer	0%	0%	
		Metal works - doors & windows	0%	0%	
		Wood works - joinery & doors	0%	0%	
		Wood works - kitchens & closets	0%	0%	
		Polishing works	0%	0%	
	Paint works - final coat	0%	0%		
	Epoxy - final coat	0%	0%		
	MEP	Drainage system UPVC	70%	70%	
		PPR - wet areas	0%	0%	
		GS - dry areas	0%	0%	
		Duct installation	60%	60%	
		Cables and wires pulling	60%	60%	
		Fans	0%	0%	
		Sanitary fixtures installation	0%	0%	
		Wiring devices installation	100%	100%	
Lighting fixtures installation		0%	0%		
Panel Board installation		0%	0%		
Mechanical functional test		0%	0%		
Electrical functional test		0%	0%		

9th Floor	Concrete Works	Columns	100%	100%	
		Slabs	100%	100%	
	Finishes	Masonry	100%	100%	
		Lintels and jambs	100%	100%	
		Wood works - subframes	100%	100%	
		Metal works - subframes	0%	0%	
		Plastering	100%	100%	
		Paint - ceilings	0%	0%	
		Walls tiling (WCs and Kitchen)	0%	0%	
		Waterproofing - wet areas	0%	0%	
		False Ceilings	0%	0%	
		Floors tiling	0%	0%	
		Paint works – putty+primer	0%	0%	
		Metal works - doors & windows	0%	0%	
		Wood works - joinery & doors	0%	0%	
		Wood works - kitchens & closets	0%	0%	
		Polishing works	0%	0%	
	Paint works - final coat	0%	0%		
	Epoxy - final coat	0%	0%		
	MEP	Drainage system UPVC	70%	70%	
		PPR - wet areas	0%	0%	
		GS - dry areas	0%	0%	
		Duct installation	40%	0%	
		Cables and wires pulling	20%	20%	
		Fans	0%	0%	
		Sanitary fixtures installation	0%	0%	
		Wiring devices installation	100%	100%	
Lighting fixtures installation		0%	0%		
Panel Board installation		0%	0%		
Mechanical functional test		0%	0%		
Electrical functional test		0%	0%		

10th Floor	Concrete Works	Columns	100%	100%	
		Slabs	100%	100%	
	Finishes	Masonry	100%	100%	
		Lintels and jambs	100%	100%	
		Wood works - subframes	100%	100%	
		Metal works - subframes	0%	0%	
		Plastering	100%	100%	
		Paint - ceilings	0%	0%	
		Walls tiling (WCs and Kitchen)	0%	0%	
		Waterproofing - wet areas	0%	0%	
		False Ceilings	0%	0%	
		Floors tiling	0%	0%	
		Paint works – putty+primer	0%	0%	
		Metal works - doors & windows	0%	0%	
		Wood works - joinery & doors	0%	0%	
		Wood works - kitchens & closets	0%	0%	
		Paint works - final coat	0%	0%	
	Epoxy - final coat	0%	0%		
	MEP	Drainage system UPVC	50%	50%	
		PPR - wet areas	0%	0%	
		GS - dry areas	0%	0%	
		Duct installation	40%	0%	
		Cables and wires pulling	20%	20%	
Fans		0%	0%		
Sanitary fixtures installation		0%	0%		
Wiring devices installation		100%	100%		
Lighting fixtures installation		0%	0%		
Panel Board installation		0%	0%		
Mechanical functional test		0%	0%		
Electrical functional test	0%	0%			

11th Floor	Concrete Works	Columns	100%	100%	
		Slabs	100%	100%	
	Finishes	Masonry	100%	100%	
		Lintels and jambs	100%	100%	
		Wood works - subframes	100%	100%	
		Metal works - subframes	0%	0%	
		Plastering	100%	100%	
		Paint - ceilings	0%	0%	
		Walls tiling (WCs and Kitchen)	0%	0%	
		Waterproofing - wet areas	0%	0%	
		False Ceilings	0%	0%	
		Floors tiling	0%	0%	
		Paint works – putty+primer	0%	0%	
		Metal works - doors & windows	0%	0%	
		Wood works - joinery & doors	0%	0%	
		Wood works - kitchens & closets	0%	0%	
		Parquet	0%	0%	
		Polishing works	0%	0%	
		Paint works - final coat	0%	0%	
		Epoxy - final coat	0%	0%	
	MEP	Drainage system UPVC	50%	50%	
		PPR - wet areas	0%	0%	
		GS - dry areas	0%	0%	
		Duct installation	0%	0%	
		Cables and wires pulling	0%	0%	
		Fans	0%	0%	
		Sanitary fixtures installation	0%	0%	
Wiring devices installation		100%	100%		
Lighting fixtures installation		0%	0%		
Panel Board installation		0%	0%		
Mechanical functional test		0%	0%		
Electrical functional test	0%	0%			

12th Floor	Concrete Works	Columns	100%	100%	
		Slabs	100%	100%	
	Finishes	Masonry	100%	100%	
		Lintels and jambs	100%	100%	
		Wood works - subframes	0%	0%	
		Metal works - subframes	0%	0%	
		Plastering	0%	0%	
		Paint - ceilings	0%	0%	
		Walls tiling (WCs and Kitchen)	0%	0%	
		Waterproofing - wet areas	0%	0%	
		False Ceilings	0%	0%	
		Floors tiling	0%	0%	
		Paint works – putty+primer	0%	0%	
		Metal works - doors & windows	0%	0%	
		Wood works - joinery & doors	0%	0%	
		Wood works - kitchens & closets	0%	0%	
		Parquet	0%	0%	
		Polishing works	0%	0%	
		Paint works - final coat	0%	0%	
		Epoxy - final coat	0%	0%	
	MEP	Drainage system UPVC	40%	40%	
		PPR - wet areas	0%	0%	
		GS - dry areas	0%	0%	
		Duct installation	0%	0%	
		Cables and wires pulling	0%	0%	
		Fans	0%	0%	
		Sanitary fixtures installation	0%	0%	
		Wiring devices installation	0%	0%	
Lighting fixtures installation		0%	0%		
Panel Board installation		0%	0%		
Mechanical functional test		0%	0%		
Electrical functional test		0%	0%		

13th Floor	Concrete Works	Columns	100%	100%	
		Slabs	100%	100%	
	Finishes	Masonry	60%	60%	
		Lintels and jambs	60%	0%	
		Wood works - subframes	0%	0%	
		Metal works - subframes	0%	0%	
		Plastering	0%	0%	
		Paint - ceilings	0%	0%	
		Walls tiling (WCs and Kitchen)	0%	0%	
		Waterproofing - wet areas	0%	0%	
		False Ceilings	0%	0%	
		Floors tiling	0%	0%	
		Paint works – putty+primer	0%	0%	
		Metal works - doors & windows	0%	0%	
		Wood works - joinery & doors	0%	0%	
		Wood works - kitchens & closets	0%	0%	
		Parquet	0%	0%	
		Polishing works	0%	0%	
		Paint works - final coat	0%	0%	
		Epoxy - final coat	0%	0%	
	MEP	Drainage system UPVC	20%	20%	
		PPR - wet areas	0%	0%	
		GS - dry areas	0%	0%	
		Duct installation	0%	0%	
		Cables and wires pulling	0%	0%	
		Fans	0%	0%	
		Sanitary fixtures installation	0%	0%	
Wiring devices installation		20%	20%		
Lighting fixtures installation		0%	0%		
Panel Board installation		0%	0%		
Mechanical functional test		0%	0%		
Electrical functional test	0%	0%			

14th Floor	Concrete Works	Columns	100%	100%	
		Slabs	100%	100%	
	Finishes	Masonry	10%	10%	
		Lintels and jambs	0%	0%	
		Wood works - subframes	0%	0%	
		Metal works - subframes	0%	0%	
		Plastering	0%	0%	
		Paint - ceilings	0%	0%	
		Floors grinding	0%	0%	
		Walls tiling (WCs and Kitchen)	0%	0%	
		Waterproofing - wet areas	0%	0%	
		False Ceilings	0%	0%	
		Floors tiling	0%	0%	
		Paint works – putty+primer	0%	0%	
		Metal works - doors & windows	0%	0%	
		Wood works - joinery & doors	0%	0%	
		Wood works - kitchens & closets	0%	0%	
		Parquet	0%	0%	
		Polishing works	0%	0%	
		Paint works - final coat	0%	0%	
	Epoxy - final coat	0%	0%		
	MEP	Drainage system UPVC	0%	0%	
		PPR - wet areas	0%	0%	
		GS - dry areas	0%	0%	
		Duct installation	0%	0%	
		Cables and wires pulling	0%	0%	
		Fans	0%	0%	
		Sanitary fixtures installation	0%	0%	
Wiring devices installation		0%	0%		
Lighting fixtures installation		0%	0%		
Panel Board installation		0%	0%		
Mechanical functional test		0%	0%		
Electrical functional test		0%	0%		

b. Safety Management

OBJECTIVES

The objective of DOLMEN CONTRACTING (DC) is to control or minimize lost time injuries/accidents (LTI/A) in all project operations, and to promote an accident and injury-free (AIF) culture. Our goals are to identify and follow the most suitable and applicable local and international standards in the construction industry within a STEP CHANGE approach and to preserve a safe work environment. Our mission is to protect the Health and Safety of personnel involved in project operations while minimizing damage caused to the environment by controlling the hazards and impacts.

DC has been thoroughly monitoring all necessary procedures and the relevant implementations by the contractor. Simultaneously, ID explained to all project teams, that by complying with the occupational HSE Regulations, they also need to filter down to all laborers and operators and not only be discussed at the executive level. As a general rule, **safety is everyone's responsibility throughout the project life cycle.**

SUMMARY OF HSE REPORT

Safe Work Procedures that are reasonably practicable have been applied for most of **the project activities so far and have minimized the risk of employees' Health, Safety and Environment.**

REPORT:

Appended is the health and safety report that was provided by the health and safety department for the correspondent month of June 2013.

3. PHOTOS

The following section provides some indicative idea on progress of works that were conducted by the main contractor.

They are not necessarily demonstrating all activities of works that were carried out during the period of the report.





Progress of works on the 1st floor





Progress of works on the 3rd floor





Progress of works on the 5th floor





Progress of works on the 6th floor





Progress of works on the 8th floor





Progress of works on the 9th floor





Progress of works on the 11th floor





Progress of works on the 12th floor



